

3. PROJECT PLANNING PHASE


ServiceNow-Based Employee Laptop Request Application

Prepared By: Nadakuditi Bindu

3.1 Planning Objective

The planning phase organizes implementation into manageable activities and defines the sequence in which the application components should be configured, validated and prepared for deployment.

3.2 Project Planning Workflow

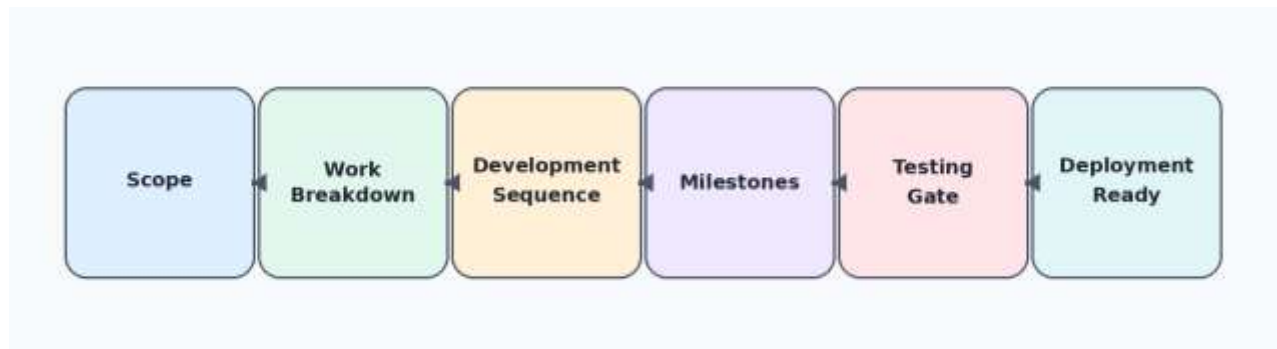

3.3 Work Breakdown Structure

Phase	Work Package	Output
1	Application foundation	Scoped application + Update Set
2	Data model	Laptop Request table + fields
3	Request interface	Laptop Request Record Producer
4	Backend validation	Laptop Request Business Rule
5	Automation	Flow Designer approval process
6	Security	Roles + Groups + ACLs
7	Validation	Functional + security testing
8	Deployment preparation	Update Set ready for deployment

3.4 Development Sequence

- Create and make the Update Set current.
- Create the custom scoped application.
- Create the Laptop Request table and fields.
- Create and map the Record Producer.
- Configure the annual duplicate Business Rule.
- Build the Flow Designer approval process.
- Configure roles, groups and ACLs.
- Execute functional and security validation.
- Confirm deployment readiness through the Update Set.

3.5 Milestone Plan

Milestone	Completion Evidence
M1 – Foundation	Application and Update Set created
M2 – Data Model	Custom table and fields configured
M3 – Request Entry	Record Producer mapped and available in Employee Service Catalog
M4 – Validation	Business Rule tested
M5 – Automation	Manager approval flow tested
M6 – Security	Roles, groups and ACLs tested
M7 – Quality Gate	Functional and security scenarios passed
M8 – Deployment	Configuration captured in Update Set

3.6 Project Roles

Role	Responsibility
Employee	Submit and manage permitted laptop request records.
IT Manager	Review requests and provide approval decisions.
Project / Development Team	Configure application, logic, automation and security; perform validation.

3.7 Planning Controls

- Keep configuration changes within the current Update Set.
- Validate table-to-Record Producer mappings before testing.
- Test duplicate prevention before approval automation.
- Validate both approval outcomes.
- Test employee and manager permissions separately.
- Use defined test scenarios as the quality gate before deployment.

3.8 Planning Deliverables

The planned outcome is a controlled, testable ServiceNow application with a clear implementation sequence. The planning structure separates configuration work from validation work so that each major capability can be checked before the project is considered deployment-ready.
